


Project: Poipu Road schedule 202 Date: Mon 7/5/21	Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
	Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
	Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

ID	% Complete	Task Name	Duration	Start	Finish	Predecessors																																		
							2016				2017				2018				2019				2020				2021				2022				2023				2024	
							Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
111	0%	HDOT Review/Approval of PS&E	30 days	Tue 3/15/22	Mon 4/25/22	48,109																																		
112	0%	ROW Certification by HDOT & FHWA	30 days	Mon 3/21/22	Fri 4/29/22	89,109																																		
113	0%	Obligation Pkg to HWY-SM via HDOT PM	5 days	Mon 5/2/22	Fri 5/6/22	112,111																																		
114	0%	FHWA Obligation	80 days	Mon 5/9/22	Fri 8/26/22	113																																		
115	0%	Project Out to Bid	36 days	Mon 10/10/22	Mon 11/28/22	114FS+30 day																																		
116	0%	Bid Award	1 day	Tue 11/29/22	Tue 11/29/22	115																																		
117	0%	Contract Negotiation with Contractor	55 days	Wed 11/30/22	Tue 2/14/23	116																																		
118	0%	Notice to Proceed issued to Contractor	1 day	Wed 2/15/23	Wed 2/15/23	117																																		
119	0%	Construction of Improvements	543 days	Tue 4/18/23	Thu 5/15/25																																			
120	0%	Start of Construction	1 day	Tue 4/18/23	Tue 4/18/23	118FS+43 day																																		
121	0%	Substantial Completion	1 day	Wed 9/4/24	Wed 9/4/24	120FS+360 day																																		
122	0%	Plant Establishment Period	180 days	Thu 9/5/24	Wed 5/14/25	121																																		
123	0%	Final Acceptance	1 day	Thu 5/15/25	Thu 5/15/25	122																																		
124	0%	Project Closeout	13 mons	Thu 9/5/24	Wed 9/3/25	121																																		

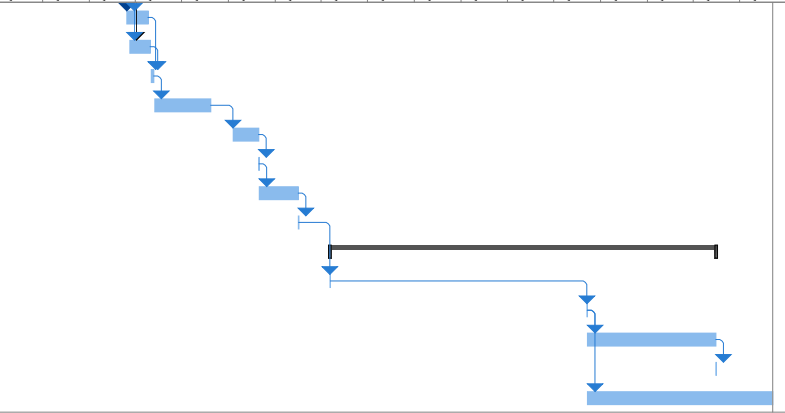

Project: Poipu Road schedule 202
Date: Mon 7/5/21

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			
